

Example project

Work breakdown and delivery review

Illustrative example - not an approved project schedule

Owner: Unassigned Window: 2026-10-05 to 2026-11-30 Source fingerprint: 3db6c1b73da38213

Baseline: Fictional example for template demonstration

How to read this review

Part	What it tells you
1 Work hierarchy	Groups organize numbered work packages.
2 Package definition	Deliverable, owner, dependencies, and completion evidence.
3 Dates and dependencies	Calendar windows and finish-to-start prerequisites.
4 Lifecycle stages	The colored steps inside a work package.
5 Releases and gates	Delivery membership, readiness checkpoints, and acceptance evidence.
6 Requirement coverage	Every supplied requirement has one primary package, including later scope.

Scope at a glance


Disposition	Requirements
Current	6
Deferred	1

Structural checks passed for the supplied data. This does not approve scope, confirm estimates, or prove completeness against evidence not supplied. End dates are exclusive boundaries. Arrows show finish-to-start dependencies when both endpoints are in the same timeline panel; all dependencies are listed in the dictionary.

Grouped delivery roadmap

2026-10-05 to 2026-11-30 · package rows 1–6 of 6

WBS / WORK PACKAGE

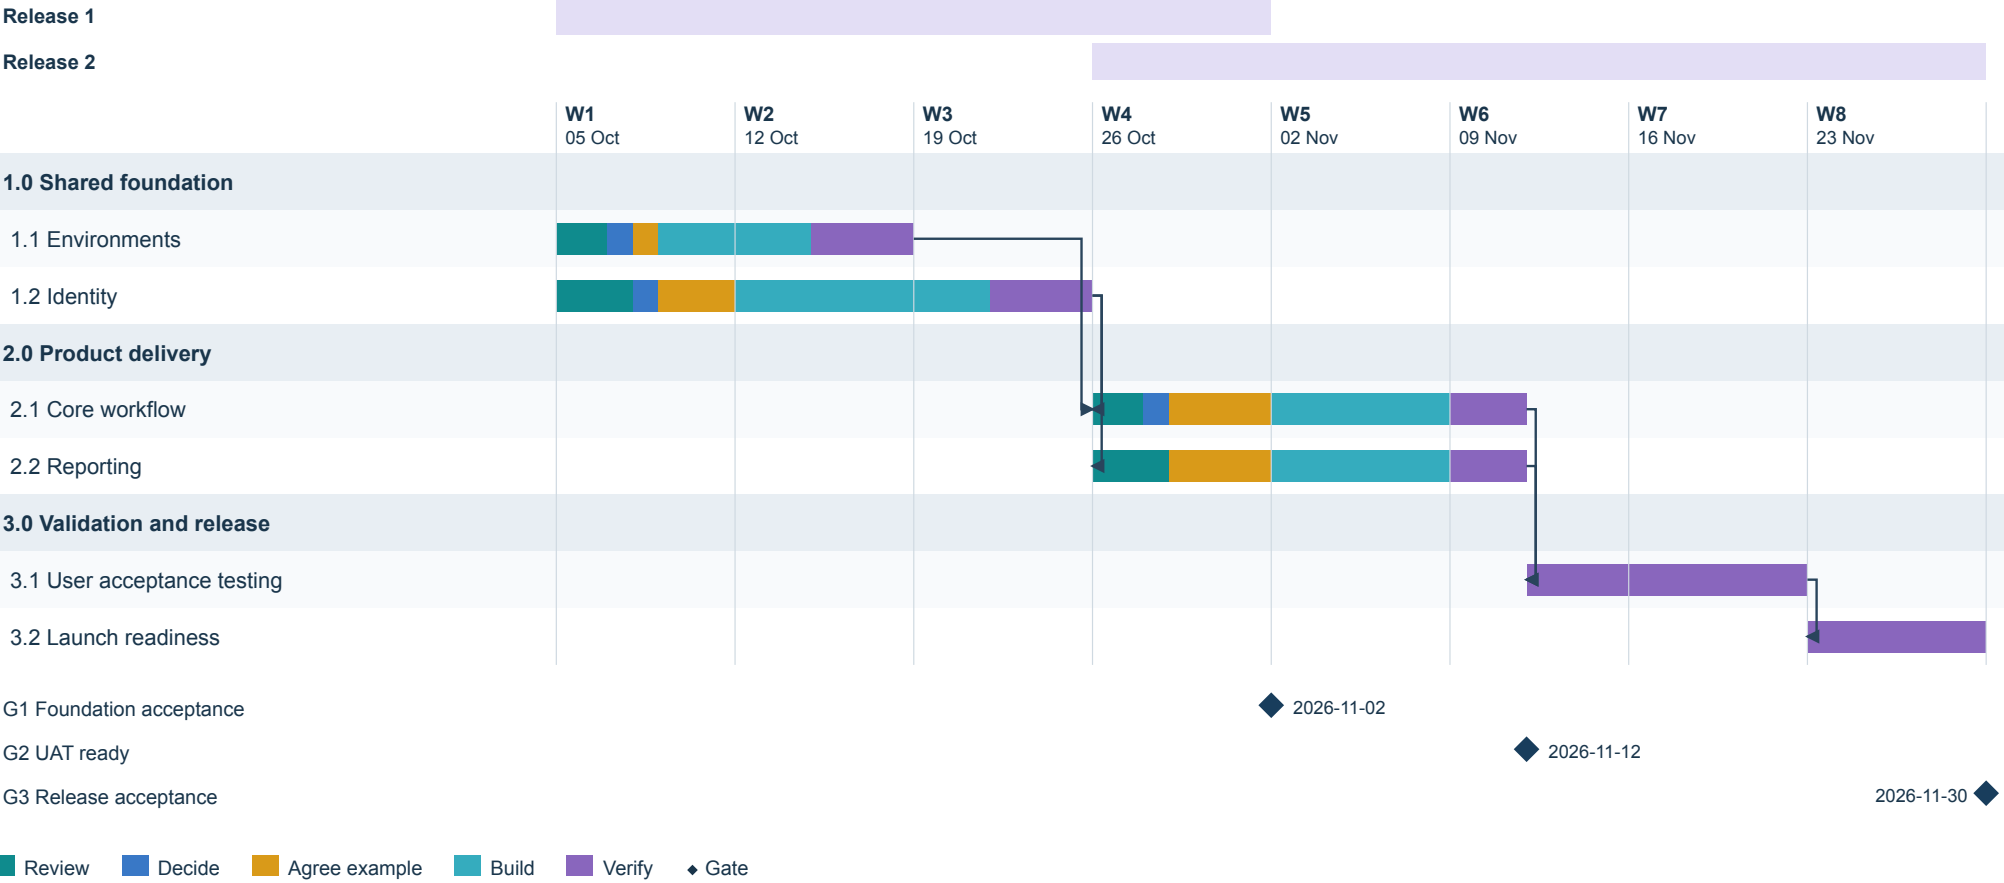

Scheduled work package dictionary

1.0 Shared foundation

1.1 Environments

Current · Release 1 · 2026-10-05 to 2026-10-19

Deliverable: A working build and deployment environment.

Owner: Platform team

Done when: Deploy a sample build and demonstrate recovery.

Depends on: None

Requirements: REQ-001

Stages: Review 2026-10-05 to 2026-10-07 · Decide 2026-10-07 to 2026-10-08 · Agree example 2026-10-08 to 2026-10-09 · Build 2026-10-09 to 2026-10-15 · Verify 2026-10-15 to 2026-10-19

1.2 Identity

Current · Release 1 · 2026-10-05 to 2026-10-26

Deliverable: Role-based access for the example application.

Owner: Platform team

Done when: Approved role scenarios pass access checks.

Depends on: None

Requirements: REQ-002

Stages: Review 2026-10-05 to 2026-10-08 · Decide 2026-10-08 to 2026-10-09 · Agree example 2026-10-09 to 2026-10-12 · Build 2026-10-12 to 2026-10-22 · Verify 2026-10-22 to 2026-10-26

2.0 Product delivery

2.1 Core workflow

Current · Release 2 · 2026-10-26 to 2026-11-12

Deliverable: One complete operating workflow with retained history.

Owner: Product team

Done when: The agreed end-to-end example passes with evidence retained.

Depends on: 1.1, 1.2

Requirements: REQ-003

Stages: Review 2026-10-26 to 2026-10-28 · Decide 2026-10-28 to 2026-10-29 · Agree example 2026-10-29 to 2026-11-02 · Build 2026-11-02 to 2026-11-09 · Verify 2026-11-09 to 2026-11-12

2.2 Reporting

Current · Release 2 · 2026-10-26 to 2026-11-12

Deliverable: An operational report using the agreed record definitions.

Owner: Product team

Done when: Report values reconcile to the agreed sample records.

Depends on: 1.2

Requirements: REQ-004

Stages: Review 2026-10-26 to 2026-10-29 · Agree example 2026-10-29 to 2026-11-02 · Build 2026-11-02 to 2026-11-09 · Verify 2026-11-09 to 2026-11-12

3.0 Validation and release

3.1 User acceptance testing

Current · Release 2 · 2026-11-12 to 2026-11-23

Deliverable: Reviewed acceptance scenarios and recorded results.

Owner: Business reviewers

Done when: Required scenarios pass or receive explicit recorded disposition.

Depends on: 2.1, 2.2

Requirements: REQ-005

Stages: Verify 2026-11-12 to 2026-11-23

3.2 Launch readiness

Current · Release 2 · 2026-11-23 to 2026-11-30

Deliverable: A reviewed release and rollback decision.

Owner: Release owner

Done when: Acceptance evidence, support readiness, and rollback are reviewed.

Depends on: 3.1

Requirements: REQ-006

Stages: Verify 2026-11-23 to 2026-11-30

Release gates and acceptance evidence

Gate	Date / release	Prerequisites	Owner / status	Required evidence
G1 Foundation acceptance	2026-11-02 / Release 1	1.1, 1.2	Release owner / Pending	Environment and identity checks pass.
G2 UAT ready	2026-11-12 / Release 2	2.1, 2.2	Business reviewers / Pending	Workflow and report verification is complete.
G3 Release acceptance	2026-11-30 / Release 2	3.1, 3.2	Release owner / Pending	Acceptance and operational readiness evidence is reviewed.

Unscheduled work package dictionary

Later, optional, and excluded scope remains outside the delivery roadmap.

Group / package	Disposition / owner	Deliverable	Condition before delivery	Requirements
Later optional and excluded scope / 4.1 Historical archive	Deferred / Unassigned	Potential later historical-record import.	Scope and acceptance criteria must be agreed before scheduling.	REQ-007

Review response

Response: Accept / Accept with recorded changes / Needs discussion

Reviewer and date: _____

Requested changes and affected IDs: _____

Approval record: _____

Requirement coverage

One primary package per supplied requirement. Statements and source references are retained below.

Requirement	Exact statement	Primary package	Disposition / release	Source
REQ-001 Deployment environment	The system shall support a repeatable deployment process.	1.1	Current / Release 1	Fictional baseline section 1
REQ-002 Role-based access	The system shall enforce the agreed role permissions.	1.2	Current / Release 1	Fictional baseline section 2
REQ-003 Operating workflow	The system shall retain the history of the operating workflow.	2.1	Current / Release 2	Fictional baseline section 3
REQ-004 Operational report	The system shall report the agreed operating totals.	2.2	Current / Release 2	Fictional baseline section 4
REQ-005 Acceptance evidence	The release shall retain acceptance scenario results.	3.1	Current / Release 2	Fictional baseline section 5
REQ-006 Rollback readiness	The release shall include a reviewed rollback procedure.	3.2	Current / Release 2	Fictional baseline section 6
REQ-007 Historical import	A later scope may import historical records after explicit approval.	4.1	Deferred / Not scheduled	Fictional baseline section 7
